



University of Colorado
Anschutz Medical Campus

The Anschutz Health Sciences Building

Construction Update
15 July 2019

CAAICON

- 
- Construction Status
 - Accomplishments to Date
 - Upcoming Activities

Agenda

Project Leadership and Staff



Doug Wilson, Project Director
doug.wilson@caaicon.com

Daniel Loosbrock, Project Executive
daniel.loosbrock@caaicon.com



Eric Snelling, Senior Superintendent



University of Colorado
Anschutz Medical Campus

David Turnquist, Associate Vice Chancellor
Facilities Management

Michael Barden, Director
Facilities Projects

Ethan Carter, PhD, Director
Department of Environmental Health and Safety

Breanne Beck, Senior Industrial Hygienist
Department of Environmental Health and Safety

LoriAnn Smith, Associate Director
University Risk Management


An aerial photograph of a large university campus, showing a dense arrangement of academic buildings, dormitories, and green spaces. The image is in grayscale. Overlaid on the center of the image is the text "Construction Status" in a large, black, sans-serif font.

Construction Status



Construction Progress

- Caissons Complete
- Foundation Walls
- Elevator/ Stair Cores
- Underground Plumbing
- Backfill Along Foundation Walls

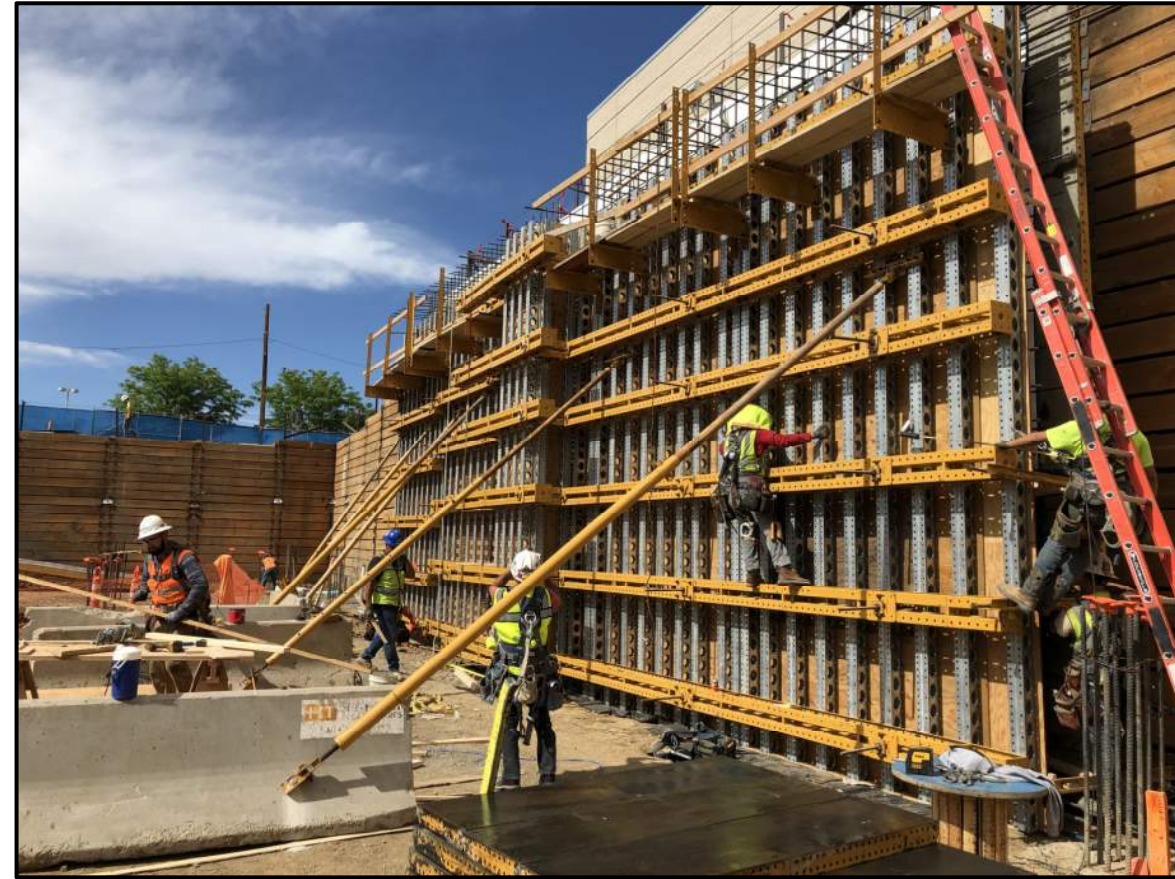

An aerial, grayscale photograph of a large university campus. The image shows a dense collection of academic buildings, dormitories, and administrative structures. There are several large, open green spaces, including what appears to be a baseball field on the left and various lawns and parks throughout the campus. Roads and parking lots are visible, weaving between the buildings. The overall layout is organized and sprawling. Overlaid in the center of the image is the text "Upcoming Activities" in a large, bold, black sans-serif font.

Upcoming Activities

Plumbing and Electrical UG

Foundation Walls, Columns, SOG

Level 1 Concrete- August

Start going vertical with decks after Level 1 complete.

North Tunnel- On Hold. Team mitigating infiltration prior to work starting.

North Tunnel- On Hold. Team mitigating infiltration prior to work starting.

19th

R2 DOCK

R2

Tower Crane

South Tunnel

ART WALK

17th

FIRE LANE ACCESS

WALKWAY

Reminders

- Next Town Hall
 - August 7th at 12:00pm
- Information can be found on the Facilities Active Projects website:
<http://www.ucdenver.edu/about/departments/FacilitiesManagement/FacilitiesProjects/ActiveProjects/Pages/AnschutzHealthSciencesBldg.aspx>
- Contact Information
 - Doug Wilson, doug.wilson@caaicon.com

An aerial photograph of a large university campus, likely the University of Illinois at Urbana-Champaign, showing various academic buildings, a central quad, and surrounding infrastructure. The image is in grayscale and has a slightly faded, artistic quality. The word "Questions?" is superimposed in a large, black, sans-serif font on the left side of the image.

Questions?
